
GENERAL NOTES:

1. THE TOTAL AREA OF THE PARCEL IS 8.06 ACRES.
2. THE PARCEL IS LOCATED WITHIN THE R ZONING DISTRICT.
3. WETLAND BOUNDARIES SHOWN ARE AS FIELD DELINEATED BY R. RICHARD SNARSKI, C.P.S.S. MARLBOROUGH, CONNECTICUT.
4. THE PARCEL IS IDENTIFIED ON THE TAX ASSESSOR'S MAPS AS MAP 81 LOT 32.
5. WETLAND BOUNDARY FLAGS WERE FIELD SURVEYED BY RICHARD W. GATES, L.S. CENTERBROOK, CONNECTICUT.
6. THIS PARCEL IS NOT LOCATED WITHIN A 100 YEAR FLOOD HAZARD ZONE.
7. BOUNDARY AND TOPOGRAPHIC SURVEY INFORMATION BASED ON MAP ENTITLED "WORKSHEET OF LAND OF DAVID W. SHELBERG & JOANNE SHELBERG NORTH MOODUS ROAD, EAST HADDAM, CONNECTICUT" DATED NOV. 19, 2024 AS PREPARED BY RICHARD W. GATES, CENTERBROOK, CONNECTICUT.

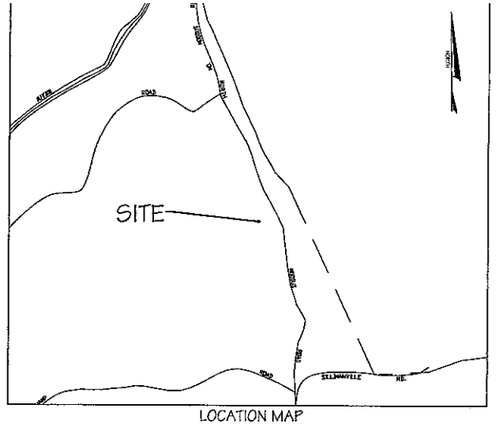

LOCATION MAP
SCALE: 1"=1000'

SOIL TEST RESULTS (11-14-24)
MAP 81 LOTS 32
NORTH MOODUS ROAD
EAST HADDAM, CONNECTICUT

CONDUCTED BY RACHEL COLONNI, CHATHAM HEALTH DISTRICT AND NEMERGUT CONSULTING

DEEP TEST HOLE 1
0" - 8" TOPSOIL
8" - 21" YELLOW BROWN FINE SANDY LOAM
21" - 35" LIGHT BROWN FINE SILTY SAND
35" - 80" GREY VERY FINE SAND AND STONES
MOTTLES: 35"
GW: NONE
LEDGE: NONE
ROOTS: 35"
RESTRICTIVE: 35"

DEEP TEST HOLE 2
0" - 12" TOPSOIL
12" - 45" YELLOW BROWN FINE SANDY LOAM
45" - 78" GREY VERY FINE SAND AND STONES
MOTTLES: 40"
GW: NONE
LEDGE: NONE
ROOTS: 35"
RESTRICTIVE: 40"

DEEP TEST HOLE 3
0" - 8" TOPSOIL
8" - 27" YELLOW BROWN FINE SANDY LOAM
27" - 45" LIGHT BROWN FINE SILTY SAND
45" - 78" GREY VERY FINE SAND AND STONES
MOTTLES: 37"
GW: NONE
LEDGE: NONE
ROOTS: 35"
RESTRICTIVE: 37"

DEEP TEST HOLE 4
0" - 9" TOPSOIL
9" - 22" YELLOW BROWN FINE SANDY LOAM
22" - 54" LIGHT BROWN FINE SILTY SAND
54" - 77" GREY VERY FINE SAND AND STONES
MOTTLES: 32"
GW: NONE
LEDGE: NONE
ROOTS: 38"
RESTRICTIVE: 32"

NOTE:
THERE ARE NO EXISTING WELLS WITHIN 75 FEET OF THE PROPOSED SEPTIC SYSTEM AND NO EXISTING SEPTIC SYSTEMS LOCATED WITHIN 75 FEET OF THE PROPOSED WELL.

NOTE:
PRIOR TO CONSTRUCTION, THE CONTRACTOR SHALL CONTACT THE PROJECT SURVEYOR, RICHARD GATES @ (860) 767-0778 TO SET A PROJECT BENCHMARK ADJACENT TO THE PROPOSED SEPTIC SYSTEM.

N/F
Patricia M. Distefano

LEGEND:
EXISTING CONTOUR
PROPOSED CONTOUR
DEEP TEST HOLE
PERCOLATION TEST
SILT FENCE/WOOD CHIP BERM
LIMIT OF UPLAND REVIEW ZONE

PRELIMINARY - FOR REVIEW ONLY

SCALE: 1" = 20 FEET

NEMERGUT CONSULTING
235 ROUTE 20 - P.O. BOX 666
KILLINGWORTH, CONNECTICUT 06419
PHONE: 860.663.2384
NEMERGUTCONSULTING.COM

ROGER D. NEMERGUT
PROFESSIONAL ENGINEER
LIC. NO. 10006

JASON A. NEMERGUT
PROFESSIONAL ENGINEER
LIC. NO. 26088

COPYRIGHT © 2025 NEMERGUT CONSULTING

NEMERGUT CONSULTING RESERVES ITS COMMON LAW COPYRIGHT AND OTHER PROPERTY RIGHTS IN THESE PLANS. THESE DOCUMENTS ARE NOT TO BE REPRODUCED, CHANGED OR COPIED IN ANY FORM OR MANNER WHATSOEVER NOR ARE THEY TO BE ASSIGNED TO A THIRD PARTY WITHOUT FIRST OBTAINING THE EXPRESSED WRITTEN PERMISSION OF NEMERGUT CONSULTING

THIS DRAWING SHALL NOT BE USED FOR CONSTRUCTION UNLESS THE DESIGN ENGINEER'S RAISED PROFESSIONAL SEAL APPEARS ON THE PLAN; AND THE OWNER/CONTRACTOR HAS CONTACTED THE DESIGN ENGINEER TO VERIFY THAT THEY ARE IN POSSESSION OF THE LATEST APPROVED DESIGN PLANS.

SITE PLAN & EROSION AND SEDIMENT CONTROL PLAN

DAVID SHELBERG
J.P.N. CONSTRUCTION LLC.
NORTH MOODUS ROAD
EAST HADDAM CONNECTICUT


MAP: 81 LOT: 32

DATE: 12-12-24
DESIGNED BY: J.A.N.
CHECKED BY: R.D.N.
SCALE: 1" = 20'

NO.	DATE	REVISIONS

SHEET

1 OF 2



"H= 6" (GST6208)
12" (GST6212)
18" (GST6218)
24" (GST6224)
30" (GST6230)
36" (GST6236)

"P= 5.5"

*3" min. I.D., ASTM D-3034, SDR 35 pipe for gravity applications


GEOMATRIX CONTACT INFORMATION:
DAVID POTTS (GEOMATRIXLLC.COM)
860-227-0686

GEOMATRIX GST LEACHING SYSTEM


B-B' CROSS SECTION

ASTM C-33 SAND SPECIFICATIONS

SIEVE SIZE	SPECIFICATION PERCENT PASSING DRY SIEVE
0.375"	100.0-100.0
#4	95.0 – 100.0
#8	80.0 – 100.0
#16	50.0 – 85.0
#30	25.0 – 60.0
#50	5.0 – 30.0
#100	< 10.0
#200	< 3.0



TOP VIEW




SIDE VIEW
(SECTION A-A)

SEPTIC TANK DETAIL

NOT TO SCALE


SEPTIC TANK SHALL BE 1,000 GALLON AS MANUFACTURED BY UNITED CONCRETE PRODUCTS, INC. YALESVILLE, CT (203-269-3161)

LIQUID CAPACITY	A LENGTH	B WIDTH	C INVERT	D HEIGHT
1000 Gal.	8'-2"	4'-6"	5'-2"	5'-11"
1000 Gal. Low Boy	9'-5 3/4"	5'-5 1/2"	3'-9 1/2"	4'-6"
1250 Gal.	9'-6 1/2"	5'-6 1/2"	4'-7"	5'-5"
1250 Gal. Heavy Duty	10'-1"	7'-7"	3'-5"	4'-7"
1500 Gal.	9'-7"	5'-6 3/4"	5'-5 3/8"	6'-3"
1500 Gal. Heavy Duty	10'-1"	7'-7"	4'-2"	5'-4"

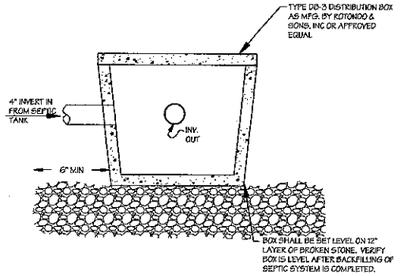

DISTRIBUTION BOX DETAIL

NOT TO SCALE



SILT FENCE DETAIL

NOT TO SCALE

EROSION AND SEDIMENT CONTROL NARRATIVE

PROJECT DESCRIPTION:

THE PROJECT CONSISTS OF THE CONSTRUCTION OF A THREE BEDROOM SINGLE FAMILY RESIDENCE AND SUPPORTING UTILITIES WITHIN THE UPLAND REVIEW AREA OF A WETLAND.

DESCRIPTION OF EXISTING SITE CONDITIONS:

THE PARCEL IS A 3.08 ACRE LOT, LOCATED ON THE WEST SIDE OF NORTH MOODUS ROAD. THERE IS AN INLAND WETLAND LOCATED IN THE CENTER AND SOUTHWESTERN PORTION OF THE LOT. THE PARCEL SLOPES GENTLY FROM EAST TO WEST. THE PROPOSED HOUSE SITE IS CURRENTLY LIGHTLY WOODED.

CONSTRUCTION SCHEDULE:

CONSTRUCTION WOULD COMMENCE LATER THIS YEAR (DEPENDING ON THE DATE OF FINAL PLAN APPROVALS) AND BE COMPLETED BY THE SUMMER OF 2025.

RECOMMENDED SEQUENCE OF CONSTRUCTION

1. INSTALL EROSION AND SEDIMENT CONTROL MEASURES AS SHOWN ON THE APPROVED SITE PLAN.
2. THE CONTRACTOR SHALL NOTIFY THE LAND USE ADMINISTRATOR AFTER THE EROSION AND SEDIMENT CONTROL MEASURES ARE IN PLACE AND AT LEAST 48 HOURS PRIOR TO THE START OF CONSTRUCTION.
3. COMMENCE CLEARING AND GRUBBING OPERATIONS AND STOCKPILE TOPSOIL. STUMPS ARE TO BE DISPOSED OF OFF SITE.
4. ROUGH IN DRIVEWAY
5. COMMENCE FOUNDATION EXCAVATION
6. POUR HOUSE FOUNDATION.
7. INSTALL FOOTING DRAINS AND BACKFILL FOUNDATION.
8. COMMENCE HOUSE CONSTRUCTION.
9. INSTALL UNDERGROUND UTILITY SERVICES.
10. INSTALL SEPTIC SYSTEM
11. DRILL WELL.
12. COMPLETE HOUSE CONSTRUCTION.
13. GRADE YARD.
14. TOPSOIL SEED AND MULCH YARD.
15. PLACE FINAL WEARING COURSE ON DRIVEWAY.
16. REMOVE EROSION CONTROL MEASURES IMMEDIATELY AFTER A PERMANENT VEGETATIVE COVER HAS BEEN ESTABLISHED ON DISTURBED AREAS.

DESIGN CRITERIA AND CONSTRUCTION DETAILS:

SEE THIS SHEET FOR CONSTRUCTION DETAILS.

FILTER FABRIC SILT FENCE AND/OR WOOD CHIP BERMS ARE TO BE USED TO INTERCEPT AND CONTAIN SOIL EROSION RESULTING FROM SURFACE RUNOFF OVER TEMPORARILY DISTURBED AREAS.

ANTI-TRACKING PAD (BROKEN STONE WHEEL CLEANER) IS TO BE INSTALLED AT TEMPORARY CONSTRUCTION ENTRANCE TO SHAKE SILT OFF OF CONSTRUCTION VEHICLE TIRES AND MINIMIZE THE AMOUNT OF SILT TRACKED ONTO THE TOWN ROAD.

MAINTENANCE PROGRAM:

FILTER FABRIC SILT FENCE AND/OR WOOD CHIP BERMS ARE TO BE INSPECTED WEEKLY AND IMMEDIATELY AFTER A RAINFALL EVENT OF 1" OR MORE IN A 24 HOUR PERIOD AND DURING A MAJOR STORM EVENT.
(A MAJOR STORM EVENT IS DEFINED AS A STORM PREDICTED BY THE NATIONAL OFFICE OF ATMOSPHERIC ADMINISTRATION WEATHER SERVICE WITH WARNINGS OF FLOODING, SEVERE THUNDERSTORMS, OR SIMILARLY SEVERE WEATHER CONDITIONS.
REPAIR OR REPLACE SILT FENCE/WOOD CHIP BERMS AS NECESSARY. CLEAN ACCUMULATED SILT AWAY FROM SILT FENCE/WOOD CHIP BERMS WHEN A DEPTH OF 6" IS REACHED OR AS NECESSARY TO MAINTAIN STRUCTURAL INTEGRITY AND EFFECTIVENESS.

ANTI - TRACKING PAD SHALL BE INSPECTED DAILY AND RENEWED WITH ADDITIONAL LAYERS OF BROKEN STONE AS REQUIRED TO MAINTAIN ITS EFFECTIVENESS.

THE PERSON RESPONSIBLE FOR OVERSEEING AND MONITORING OF THE EROSION AND SEDIMENT CONTROL MEASURES IS THE OWNER, DAVID SHELBURG, 860-301-8604.

EROSION AND SEDIMENT CONTROL NOTES:

1. ALL WORK SHALL BE PERFORMED IN COMPLIANCE WITH THESE DRAWINGS AND CONDITIONS OF THE EAST HADDAM PLANNING AND ZONING COMMISSION.
2. WORK RELATING TO EROSION AND SEDIMENT CONTROL MEASURES SHALL CONFORM TO THE DETAILS AND CONSTRUCTION METHODS ON THESE DRAWINGS AND AS OUTLINED IN THE 2002 CONNECTICUT GUIDELINES FOR SOIL EROSION AND SEDIMENT CONTROL" PUBLISHED BY THE CONNECTICUT COUNCIL ON SOIL AND WATER CONSERVATION.
3. EROSION AND SEDIMENT CONTROL DEVICES SHALL BE INSTALLED PRIOR TO THE COMMENCEMENT OF EXCAVATION OR FILL OPERATIONS IN UPHILL AREAS.
4. ALL WORK DISTURBED BY CONSTRUCTION SHALL BE TOPSOILED (6" MINIMUM DEPTH), SEEDED AND MULCHED AS SOON AS PRACTICABLE AFTER THE COMPLETION OF CONSTRUCTION IN THAT AREA. NATURAL VEGETATION IN UNDISTURBED AREAS SHALL BE RETAINED AND PROTECTED.
5. ALL SLOPES IN CUT AND FILL AREAS SHALL BE 2:1 OR MAXIMUM UNLESS NOTED OTHERWISE ON THE PLAN.
6. EROSION AND SEDIMENT CONTROL DEVICES SHALL NOT BE REMOVED UNTIL A PERMANENT VEGETATIVE COVER IS ESTABLISHED ON UPHILL AREAS.
7. RECOMMENDED SEED MIXTURE ON DISTURBED AREAS (UNLESS NOTED OTHERWISE ON THE SITE PLAN) SHALL BE: CREEPING RED FESCUE (PENN LAWN, WINTERGREEN) - 1.90 LBS PER 1000 S.F.; S.F.); BLUETOP (BYRDEKEN, COMMON) - 0.50 LBS.PER 1,000 S.F.; AND TALL FESCUE (KENTUCKY 31) OR SMOOTH BROMEGRASS (SARATOGA, LINCOLN) - 1.80 LBS. PER 1,000 S.F.. RECOMMENDED SEEDING DATES ARE MARCH 15 THROUGH JUNE 15 AND AUGUST 15 THROUGH OCTOBER 15. USE HAY MULCH ON ALL SEEDED AREAS FOR MOISTURE RETENTION.
8. DISTURBED AREAS SHALL NOT BE SEEDED OUTSIDE OF THE RECOMMENDED SEEDING DATES, BUT SHALL BE TEMPORARILY STABILIZED WITH HAY MULCH UNTIL A PERMANENT SEEDING DURING RECOMMENDED SEEDING DATES CAN TAKE PLACE.
9. EROSION AND SEDIMENT CONTROL DEVICES SHALL BE INSPECTED PERIODICALLY, PARTICULARLY AFTER A RAINFALL EVENT, AND REPAIRED, MAINTAINED BY THE APPLICANT AS REQUIRED.
10. LIME AND FERTILIZER APPLICATION RATES SHALL BE BASED UPON THE RESULTS OF SOIL SAMPLE TESTS PERFORMED BY THE APPLICANT.
11. MINIMUM TOPSOIL DEPTH IN AREAS TO BE SEEDED SHALL BE 6".

1. ALL ELEVATIONS AND CONTOURS ARE BASED ON AN ASSUMED DATUM.
2. ELEVATIONS AND CONTOURS ARE BASED ON AN AS-SURVEYED DATUM.
3. ELEVATIONS SHOWN REFER TO THE INVERT (FLOW LINE) OF THE PROPOSED LEACHING SYSTEM UNLESS NOTED OTHERWISE.
4. PERCOLATION RATE FOR DESIGN = 0 - 10 MINUTES PER INCH.
5. THE MINIMUM DISTANCE FROM WELL TO SEPTIC IS 75 FEET.
6. LEACHING SYSTEM AREA SHALL BE LIMED, FERTILIZED, SEEDED AND MULCHED UPON COMPLETION OF THE PROJECT.
7. SEPTIC TANK CONSTRUCTION JOINTS SHALL BE SEALED WITH ASPHALT CEMENT. ALL PIPE CONNECTIONS TO THE SEPTIC TANK AND AND DISTRIBUTION BOXES SHALL BE SEALED WITH A POLYETHYLENE GASKET "POLY-LOK" OR APPROVED EQUAL.
8. SEPTIC TANK BAFFLES SHALL CONFORM TO SECTION YA-1 TECHNICAL STANDARDS OF THE STATE HEALTH CODE.
9. IF FIELD CONDITIONS, (LEDGE, GROUNDWATER, MOTTLING) ARE ENCOUNTERED AT AT SHALLOWER DEPTHS THAN SHOWN IN THE DEEP TEST HOLE RESULTS, CONSTRUCTION SHALL BE HALTED AND THE ENGINEER CONTACTED IMMEDIATELY.
10. SOIL TEST RESULTS SERVING AS THE BASIS FOR THIS DESIGN WERE CONDUCTED BY THE CHATHAM HEALTH DISTRICT AND NEMERGUT CONSULTING.
11. NO DEVIATIONS FROM THE APPROVED DESIGN PLAN SHALL BE ALLOWED WITHOUT THE PRIOR APPROVAL OF THE SANITARIAN OR THE DESIGN ENGINEER.
12. EROSION AND SEDIMENT CONTROL MEASURES MAY BE SUBJECT TO FIELD MODIFICATION, AS NECESSARY, AS REQUIRED BY THE DESIGN ENGINEER OR TOWN OFFICIALS.
13. STRIP AND STOCKPILE EXISTING TOPSOIL LAYER FROM WITHIN THE PROPOSED LEACHING SYSTEM IN THOSE AREAS WHERE THE BOTTOM OF THE PROPOSED LEACHING SYSTEM IS AT, OR ABOVE, THE BOTTOM OF THE EXISTING TOPSOIL LAYER OR IN THOSE AREAS WHERE SEPTIC SYSTEM FILL IS REQUIRED.
14. SELECT FILL MATERIAL SHALL MEET THE FOLLOWING REQUIREMENTS:
    A. THE FILL MATERIAL SHALL NOT CONTAIN ANY MATERIAL LARGER THAN THE THREE (3) INCH SIEVE.
    B. UP TO 40% OF THE DRY WEIGHT OF THE REPRESENTATIVE SAMPLE MAY BE RETAINED ON THE #4 SIEVE (THIS IS THE GRAVEL PORTION OF THE SAMPLE).
    C. THE MATERIAL THAT PASSES THE #4 SIEVE IS THEN REWEIGHED AND THE SIEVE ANALYSIS STARTED.
    D. THE REMAINING SAMPLES SHALL MEET THE FOLLOWING GRADATION CRITERIA:

SIEVE SIZE	PERCENT PASSING WET SIEVE	DRY SIEVE
#4	100	100
#10	70-100	70-100
#40	10-50 *	10-75
#100	0-20	0-6
#200	0-5	0-2.5

* PERCENT PASSING THE #40 SIEVE MAY BE INCREASED TO NO GREATER THAN 75% IF THE PERCENT PASSING THE #100 SIEVE DOES NOT EXCEED 10% AND THE #200 SIEVE DOES NOT EXCEED 5%.

THE FILL SHALL BE PLACED IN 12" MAXIMUM LIFTS AFTER THE STRIPPED LEACHING SYSTEM AREA HAS BEEN SCARIFIED. TRUCKS OR OTHER CONSTRUCTION EQUIPMENT SHALL NOT BE DRIVEN OVER THE SCARIFIED AREA PRIOR TO FILL PLACEMENT. PRIOR TO FILL PLACEMENT ANY SMEARED FILL AREAS SHALL BE RE-SCARIFIED.

15. PRIOR TO PLACEMENT, FILL MATERIAL SHALL BE INSPECTED AND APPROVED BY THE HEALTH DISTRICT AND THE DESIGN ENGINEER.
16. SEPTIC TANKS SHALL BE TWO COMPARTMENT TANKS WITH HEAVY DUTY STEEL HANDLES FOR MANHOLE ACCESS COVERS AND EFFLUENT FILTERS INSTALLED ON OUTLET BAFFLES.
17. ALL PIPE DOWNSTREAM OF THE OF THE SEPTIC TANK, (EXCEPT FOR LEACHING TRENCHES) SHALL BE 4" DIAMETER P.V.C. ASTM D3034 SDR 35 OR APPROVED EQUAL.
18. THE SITE CONTRACTOR SHALL CONTACT "CALL BEFORE YOU DIG" 1-800-922-4455 PRIOR TO CONSTRUCTION TO VERIFY THE EXTENT AND LOCATION OF EXISTING UNDERGROUND UTILITIES.
19. THE LEACHING SYSTEM SHALL BE PROPERLY COVERED BY THE LICENSED SYSTEM INSTALLER WITHIN TWO (2) WORKING DAYS FOLLOWING THE LOCAL HEALTH DISTRICTS FINAL INSPECTION AND APPROVAL.
20. IMMEDIATELY UPON COMPLETION OF THE SEPTIC SYSTEM INSTALLATION AND FINAL APPROVAL BY THE HEALTH DISTRICT, THE SEPTIC SYSTEM SHALL BE BACKFILLED, TOPSOILED,SEEDED AND MULCHED. THE FINAL GRADING SHALL CONFORM TO THE DESIGN PLAN AND SHALL ENSURE THAT SURFACE RUNOFF IS DIRECTED AWAY FROM THE THE LEACHING SYSTEM. EROSION AND SEDIMENT CONTROL MEASURES SHALL NOT BE REMOVED UNTIL A PERMANENT VEGETATIVE COVER IS ESTABLISHED IN DISTURBED AREAS.
21. THE PROJECT SURVEYOR SHALL BE CONTACTED PRIOR TO BACKFILLING THE SEPTIC SYSTEM TO ALLOW FOR TAKING THE NECESSARY FIELD MEASUREMENTS FOR THE PREPARATION OF AN "AS-BUILT" SEPTIC SYSTEM PLAN AS REQUIRED BY THE HEALTH DISTRICT PRIOR TO THE ISSUANCE OF A PERMIT TO DISCHARGE OR A CERTIFICATE OF OCCUPANCY.
22. NO GRADING OR OTHER DISTURBANCE OF THE AREA OF THE PROPOSED SEPTIC SYSTEM WILL BE ALLOWED PRIOR TO THE INSTALLATION. NO PARKING, EQUIPMENT STORAGE OR TRAFFIC IN THE AREA OF THE SEPTIC SYSTEM WILL BE ALLOWED.
23. PRIOR TO COMMENCEMENT OF ANY CONSTRUCTION ACTIVITY, THE SEPTIC SYSTEM SHALL BE STAKED OUT BY THE PROJECT SURVEYOR.
24. THE DISTRICT SANITARIAN AND THE ENGINEER SHALL BE CONTACTED AT LEAST 48 HOURS PRIOR TO THE BEGINNING OF CONSTRUCTION. NO PORTION OF THE SYSTEM SHALL BE COVERED WITHOUT INSPECTION AND APPROVAL OF THE SANITARIAN AND THE ENGINEER.
25. THE MINIMUM DISTANCE FROM UTILITY TRENCH (GAS/ELECTRIC/CABLE TV/TELEPHONE) TO SEPTIC SYSTEM IS 5 FEET.
26. CONSTRUCT STORM WATER SWALES, AS REQUIRED,TO DIRECT SURFACE RUNOFF AWAY FROM THE SEPTIC SYSTEM.
27. IF A LARGE CAPACITY BATHTUB IS INSTALLED THE SEPTIC TANK SHALL BE INCREASED AS FOLLOWS:
    - 100 - 200 GALLON TUB CAPACITY - ADD 250 GALLONS TO SEPTIC TANK CAPACITY
    - OVER 200 GALLON TUB CAPACITY - ADD 500 GALLONS TO SEPTIC TANK CAPACITY
28. IF A GARBAGE DISPOSAL IS INSTALLED, THE SEPTIC TANK SHALL BE INCREASED INSTALLED BY 250 GALLONS. GARBAGE DISPOSALS ARE NOT RECOMMENDED SINCE THEY INCREASE THE SOLIDS LOADING ON THE SEPTIC TANK AND MAY PREMATURELY CLOG EFFLUENT FILTER.
29. BACKWASH FROM THE WATER TREATMENT UNITS, IF REQUIRED SHALL NOT BE DISCHARGED INTO THE SEPTIC SYSTEM.
30. ALL SEPTIC TANKS AND PUMP CHAMBERS REQUIRING RISERS SHALL MAINTAIN THE ORIGINAL COVERS ON THE TANKS, HAVE RISER COVERS THAT WEIGH AT LEAST 100 LBS. OR INSTALL A SAFETY DEVICE BELOW THE RISER TO PREVENT INDIVIDUALS FROM FALLING INTO A TANK.
31. ALL BELOW GRADE TANK OR COVER HANDLES SHALL CONTAIN OR BE FITTED WITH A MATERIAL THAT CAN BE LOCATED WITH A METAL DETECTOR.

NEMERGUT CONSULTING
239 ROUTE 80 - P.O. BOX 665
KILLINGWORTH, CONNECTICUT
06419
PHONE: 860.663.2384
NEMERGUTCONSULTING.COM

ROGER D. NEMERGUT
PROFESSIONAL ENGINEER
LIC. NO. 10008

JASON A. NEMERGUT
PROFESSIONAL ENGINEER
LIC. NO. 26088

COPYRIGHT © 2024 NEMERGUT CONSULTING

NEMERGUT CONSULTING RESERVES ITS COMMON LAW COPYRIGHT AND OTHER PROPERTY RIGHTS IN THESE PLANS. THESE DOCUMENTS ARE NOT TO BE REPRODUCED, CHANGED OR COPIED IN ANY FORM OR MANNER WHATSOEVER NOR ARE THEY TO BE ASSIGNED TO A THIRD PARTY WITHOUT FIRST OBTAINING THE EXPRESSED WRITTEN PERMISSION OF NEMERGUT CONSULTING

THIS DRAWING SHALL NOT BE USED FOR CONSTRUCTION UNLESS THE DESIGN ENGINEER'S RAISED PROFESSIONAL SEAL APPEARS ON THE PLAN; AND THE OWNER/CONTRACTOR HAS CONTACTED THE DESIGN ENGINEER TO VERIFY THAT THEY ARE IN POSSESSION OF THE LATEST APPROVED DESIGN PLANS.

DETAILS & NOTES

DAVID SHELBERG
J.P.N. CONSTRUCTION LLC.
NORTH MOODUS ROAD
EAST HADDAM CONNECTICUT

MAP: 81 LOT: 32

DATE: 12-12-24
DESIGNED BY: J.A.N.
CHECKED BY: R.D.N.
SCALE: AS NOTED

NO.	DATE	REVISIONS

SHEET

2 OF 2
